Customer Onboarding

How a customer goes from signed deal to graduation and six months beyond, and who does what at every step.

Marketing Hub | Sales Hub | Service Hub | 60–90 days



Version
1.0 · November 2026

Runs in
HubSpot Work · Supered · HubSpot CRM

Owner
RevGravy Operations

CONTENTS

What's inside

01	How to use this guide	09	Automation you'll work with
02	The program at a glance	10	When things don't go to plan
03	Roles and decision rights	11	After the program
04	Where everything lives	A	Task library
05	The procedure, step by step	B	Progress measures
06	Requests	C	Training modules
07	Statuses and data rules	D	Intake questions
08	The operating rhythm	E	Technical setup checklist

01 · HOW TO USE THIS GUIDE

Read it once, then work from the steps

Chapter 05 is the procedure: thirteen steps, each with a checklist and the condition that closes it. Everything else supports it. The appendices list every task, measure, training module, intake question and setup item, so you can see what a hub includes without opening HubSpot Work.

Blank beats invented

Leave unknown values empty and create a follow-up. Never fill a number with a guess.

Evidence before Done

A task is Done when its definition of done is met and checked, not when it looks finished.

People own the customer

Agents draft, fill fields or flag. Every customer message and commitment is human.

Day 0 is payment

Start date is the day the deal reached Start Payment Received. Kickoff is Days 5–10.

One row per engagement

Every task, request and update links to its Customers row. A later onboarding gets a new row.

No silent scope

New work goes through a request, a price and an approval.


Ten phases, one customer, 60 to 90 days

Day 0 is the day payment lands. Week one is the same for every program; later dates compress for 60- and 75-day programs. Phases overlap on purpose: they are planning windows, not gates.

99
tasks in the library

58 + 1 module
Core tasks once, plus one module per hub

8
agents that draft, fill or flag

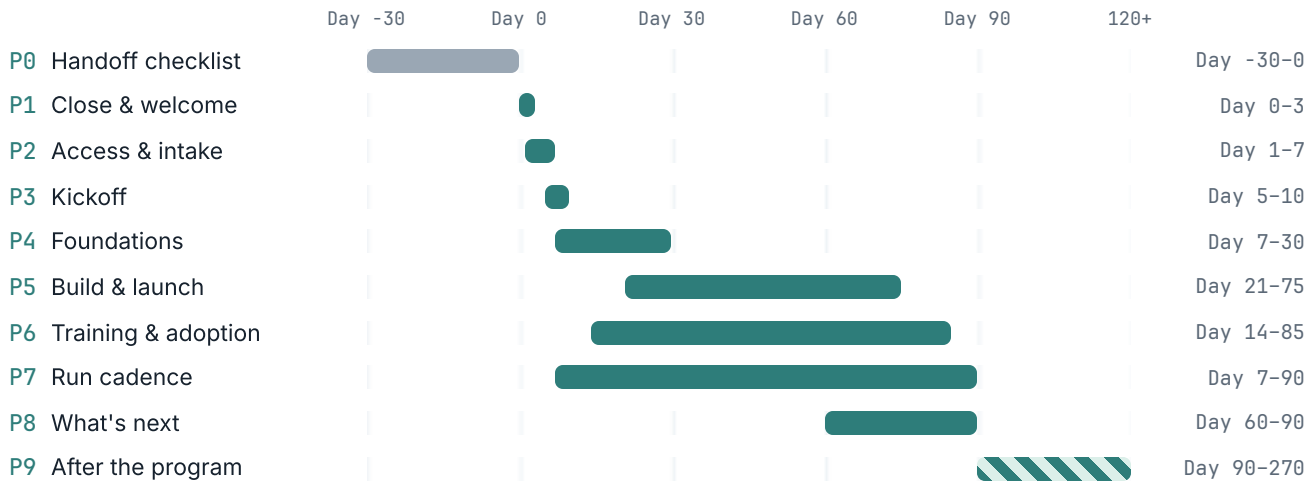

PHASE	GOAL	WHAT THE CUSTOMER SEES	DONE WHEN
P0 Handoff checklist	Everything the Architect needs is on the deal before the customer pays (Definition of Ready).	VSL, recommendation video, proposal Q&A, quote, agreement.	Deal has FigJam link, From→To statement, products, progress measures, survey, POC and supporters, signed agreement.
P1 Close & welcome	The customer feels the handoff right away; the Architect is picked and briefed within 72 hours.	Welcome email series with the Supered Action Plan (expectations, next steps, links, agreement, to-dos).	Architect assigned, Phil↔Architect 1:1 done, customer added in HubSpot Work with tasks created, kickoff booked.
P2 Access & intake	Every access and input we need arrives in week 1.	Supered announcement on how we deliver updates and documentation; one short intake form.	Portal access granted, intake submitted, audit and baseline numbers captured.
P3 Kickoff	15 minutes that confirm the plan, close gaps and set the rhythm.	Architect + team intro, confirmed plan, office hours and MBRs explained and booked.	Plan confirmed, missing items owned, MBRs on calendars, recap sent within 24h.

PHASE	GOAL	WHAT THE CUSTOMER SEES	DONE WHEN
P4 Foundations	Marketing Hub set up correctly: tracking, domains, email, data, migration, website connection, baseline dashboard.	Supered video announcements as foundation items finish; weekly updates.	Foundation QA passed, old data migrated, baseline dashboard live.
P5 Build & launch	Build each progress measure the customer bought and get it live.	A Supered video per delivery, sign-off requests, numbers moving in weekly updates.	Every progress measure is live, approved by the client and reporting.
P6 Training & adoption	The customer's team can run what we built without us.	Short Supered training videos, office-hours coaching, an admin handbook.	Each audience finished its modules; adoption checks passed.
P7 Run cadence	Same rhythm every week: office hours, Friday update, monthly business review, requests handled by urgency.	Weekly update (work done → strategic issue, numbers, issues found), office hours, MBRs.	Runs every week until the program ends.
P8 What's next	The customer sees the long-term vision and picks the next phase before the program ends.	'What's next' call with the Architect, A/B options, final results review.	Next phase chosen (A, B or KPI monitoring only), results reviewed, project closed.
P9 After the program	Keep the relationship for 6–12 more months, starting with 6 months of free KPI monitoring.	Monthly KPI snapshot, check-ins at month 3 and 6, paid offers.	Customer moved to a paid offer, or monitoring ends cleanly after 6 months.

03 · ROLES AND DECISION RIGHTS

Who does what

Phil leads through the sale and the handoff. After the handoff call the Architect is the strategy lead, including the what's next call. Owner role says who acts; Assignee is always a real internal person, even when the customer has the action.

ROLE	RESPONSIBILITY
Phil	Strategy lead through the sale and the handoff. Picks the Architect based on capacity. Reviews next-phase options.
Architect	Takes over as strategy lead after the handoff. Owns delivery, weekly updates, office hours, MBRs and the 'what's next' call.
Ops	RevGravy operations. Owns the templates, Supered setup and the welcome emails.
Client POC	Main point of contact at the customer. Owns approvals, access and client to-dos.
Supporters & decision maker	Customer people confirmed from contact labels or explicit conversations. If unclear, the role stays an open question for the handoff or kickoff.

04 · WHERE EVERYTHING LIVES

HubSpot Work runs it, Supered shows it

CRM is the source for companies, deals, contacts, quotes and products. HubSpot Work is the source for the engagement, its tasks, requests, health, measures and drafts. Supered is everything the customer sees.

TOOL	ITS JOB
HubSpot Work	The whole onboarding: one shared set of tables for all customers (Customers, Customer Task, Request, Update), a template task list, board, timeline and agents.
Supered	Everything the customer sees: Action Plan, announcements, delivery and training videos, admin handbook.
HubSpot CRM	The deal-stage gate, the two welcome emails, meetings links and the dashboards that report progress measures.

Onboarding Task Library project

Four library tables: Onboarding Library (Core, 58 tasks), Marketing Onboarding Library (16), Sales Onboarding Library (14), Service Onboarding Library (11). Templates only; nobody works in them.

Onboarding Portfolio project

Customers (one row per engagement), Customer Task (every customer's tasks), Request (every request), Update (drafts for the Architect). Every row links to its Customers row.

Customers table

COLUMN	WHAT GOES IN IT
Customer	Text: client name
Company	CRM company
Deal	CRM deal
Architect	HubSpot user
Program length	Number: 60, 75 or 90
Start date	Date: Day 0 = the day the deal reached Start Payment Received, not the kickoff date
Target end date	Date
Hub tiers	Text, e.g. Marketing Pro, Sales Enterprise
Health	Dropdown: On track, At risk, Off track
Current section	Dropdown: P0–P9, Completed
Next MBR	Date, filled by the Architect when booked
Next due task	Text
Products purchased	Multi-select: Marketing Hub Onboarding, Sales Hub Onboarding, Service Hub Onboarding
Create tasks	Checkbox: Ops ticks it to create or add tasks
Tasks created for	Multi-select, same options: set by the Task Generator
From→To goal	Long text
Progress measures	Long text: name, baseline, target
FigJam link	URL
Supered Action Plan link	URL

Step by step, from sale to six months after

Each step names when it happens, who acts, what they do, and the condition that closes it. Task IDs refer to Appendix A.

01 Prepare the sales handoff

Before Day 0 · P0 **Phil**

- [ ] Write the research brief from the company website and attach it to the deal.
- [ ] Build the FigJam canvas after the Fit call: strategic motivation, tactical outcomes, progress measures, fee range.
- [ ] Write the From→To statement: one sentence from where they are to where they want to be.
- [ ] Get the tech stack and team capacity survey back from the customer.
- [ ] Put products, quote and hub tiers on the deal. Every hub sold is Professional or Enterprise.
- [ ] Pick the progress measures for each hub sold (Appendix B), with baselines where known.
- [ ] Confirm the POC, supporters and decision maker from contact labels or explicit conversations. Never infer authority from a billing label or a job title.
- [ ] Get the agreement signed: AI terms, escalation path, how progress is measured, $250 requests with urgency classes.

Done when There is documented authority to start, scope is understood, and every missing item has a named owner. Missing evidence can carry into onboarding, but it stays visibly open.

02 Pick the Architect and add the customer

Day 0 · payment received **Phil** **Ops**

- [ ] Phil opens the Capacity report (active customers per Architect) and picks the Architect.
- [ ] Ops adds one Customers row within 4 business hours: Customer, Company, Deal, Architect, Program length (60, 75 or 90), Start date, Products purchased, Hub tiers, From→To goal, FigJam and Supered links.
- [ ] Start date is Day 0: the day the deal reached Start Payment Received. It is never the kickoff date.
- [ ] Leave unknown values blank and create a follow-up task. Blank beats invented.
- [ ] Ops ticks Create tasks.
- [ ] Welcome email #1 goes out from Phil: the Supered Action Plan, the kickoff booking link and the first to-dos.

Done when The Customers row is complete, the Company and Deal are linked, and Create tasks is ticked.

03 Create the customer's tasks

Day 0 · HubSpot Work · Ops

- [ ] The Onboarding Task Generator copies the Onboarding Library once, plus one library per product purchased, into Customer Task.
- [ ] It fills each task's Project Day 0 and Program length so the Due date formula calculates, and assigns the Architect's tasks.
- [ ] It sets Target end date, adds the products to Tasks created for, and unticks Create tasks.
- [ ] Ops checks the count: Core 58, plus Marketing 16, Sales 14, Service 11.
- [ ] If the tasks don't appear within 15 minutes, Ops copies them from the libraries by hand and fills the same fields.

Done when Tasks created for lists every product purchased, and the task count matches.

04 Run the internal handoff

Days 1–3 · Phil · Architect

- [ ] Read the Handoff Brief in the Update table. It's written from the deal's history; correct anything that's wrong before the call.
- [ ] Hold a 30-minute handoff call: what was bought, the outcome, baselines and targets, people and decision path, access needs, risks, the first customer commitment.
- [ ] The Architect walks the P0 checklist and marks each item Done only with evidence. Anything missing goes back to Phil, who fixes it within 24 hours.
- [ ] The Architect sets Won't do, with a reason, on anything the customer didn't buy (optional builds, Enterprise-only items for a Pro customer).
- [ ] The Architect writes the progress measures with baseline, target, source and owner into the Customers row.
- [ ] Every unresolved question becomes a linked task with an owner and a date.
- [ ] From here on, the Architect is the strategy lead.

Done when P0 is closed or every gap is owned, the measures are recorded, and the brief is marked Reviewed.

05 Welcome, access and intake

Days 0–7 · P1–P2 Architect Ops Customer

- [ ] Ops builds the Supered Action Plan from the template for the products bought.
- [ ] Welcome email #2 goes out on Day 2: office hours, Friday updates, how to send requests and the urgency classes, escalation path, how we use AI.
- [ ] The customer grants HubSpot access, fills the intake form, shares access to connected systems and old tools, and uploads brand files.
- [ ] Customer-owned tasks sit in Waiting on client. The Architect marks them Done only once the access works or the form is in. Silence is not access.
- [ ] Chase on Day 3. On Day 7, escalate to Phil and set Health to At risk.
- [ ] The Architect runs the portal audit and records baseline numbers.
- [ ] Credentials live only in the approved secure system, never in task notes.

Done when Access is granted, the intake is in, and baselines are recorded.

06 Kickoff

Days 5–10 · P3 Architect Customer

- [ ] Draft the agenda from the intake and the audit.
- [ ] In a 15-minute call: introduce the team; confirm the goal, scope and plan; walk through missing items; explain office hours, Friday updates, MBRs and requests.
- [ ] Book MBR #1 (about Day 30), MBR #2 (about Day 60), the what's next call (about 30 days before the end) and the final results review. Scale these for 60- and 75-day programs.
- [ ] Fill Next MBR on the Customers row. Confirm who needs which training modules.
- [ ] Send the recap within 24 hours and update the Supered plan.

Done when The plan is confirmed, the meetings are on calendars, and the recap is sent.

07 Foundations

Days 7–30 · P4 Architect

- [ ] Work through the Core foundation tasks (account, data model, import, integrations, baseline dashboard) and each hub's foundation tasks.
- [ ] A task is Done when every subtask is ticked or marked not applicable.
- [ ] Tasks blocked on the customer's IT (DNS, for example) go to Waiting on client.
- [ ] Foundation QA (4.11): test the main flow end to end for every hub sold.
- [ ] Record a Supered video: what changed for the customer and why it matters.

Done when Foundation QA passes and the baseline dashboard is live.

08 Build and launch

Days 21–75 · P5–P6 **Architect** **Customer**

- [ ] Build one progress measure at a time, in the order of the hub's library.
- [ ] A build sits in In review while it waits for the customer's sign-off, and is Done only after sign-off and go-live.
- [ ] Record a Supered video per delivery, and deliver the matching training module as each feature ships.
- [ ] Migrations: rebuild, send in parallel once, then switch the old tool off with the customer's confirmation.
- [ ] Day 45 and Day 75: adoption checks. Attendance alone is not adoption.

Done when Every progress measure sold is live, signed off and reporting.

09 Run the weekly rhythm

Day 7 to the end · P7 **Architect** **Phil** **HubSpot Work**

- [ ] Monday: the Architect plans the week from My tasks and This week.
- [ ] Every day: review overdue tasks and separate internal delays from Waiting on client.
- [ ] Friday: send the update in five parts: work done and the strategic issue it moves, numbers vs baseline, issues found outside scope, next week, the customer's to-dos. The Update row goes Draft → Reviewed → Sent.
- [ ] Set Health weekly from evidence. On track means credible; At risk means a slip is likely but recoverable; Off track means a milestone is already jeopardized.
- [ ] Phil runs a weekly delivery review with the Architects using the Health board, the Overdue view and the Capacity report.
- [ ] MBRs compare sourced actuals with baseline and target.

Done when Recurring tasks stay In progress until close-out. Each Sent update is the record that the week happened.

10 Handle requests

Any time · Architect · Customer

- [ ] Customer asks: By email, Slack, in office hours or in Supered.
- [ ] Logged the same day: The Architect adds a Requests row: Customer, Request, Type = Client request, Logged on = today.
- [ ] Agent triage: Request Triage sets Urgency, Price and Due date. A Critical request alerts the Architect and Phil.
- [ ] Customer confirms: The Architect checks the triage, then tells the customer the class, turnaround and price. Paid requests wait for their OK. Fixing something we built never does.
- [ ] Work: New → In progress once they say yes → Done. Bigger than about 2 hours → Quoted → a proposal. An idea for later → Parked.
- [ ] Billing: Ops bills every Done request with a price at the end of the month.
- [ ] What we find ourselves: Issues the Architect finds are logged as Issue found, ideas as Client idea. Both feed the Friday update and the what's next call.

Done when Done means the result is verified and communicated, with the customer's validation captured where needed.

11 What's next

About 35 to 25 days before the end · P8 · Architect · Phil

- [ ] The Architect prepares Option A and Option B from results, issues found and 'not now' ideas, and Phil reviews them.
- [ ] The Architect runs the what's next call: results so far, long-term vision, the A/B choice, and the 6 months of free KPI monitoring.
- [ ] The chosen option becomes a new deal in the Sales Pipeline.
- [ ] New work is never added silently to the original scope. It goes through a linked request and approval.

Done when The customer has chosen a next step, and the proposal is sent.

12 Graduate

`Last week of the program` Architect Ops

- [ ] Run the final results review: before vs after for every progress measure, what was built, what's still open.
- [ ] Deliver the admin handbook in Supered.
- [ ] Check the graduation gate (below). Mark every remaining task Done or Won't do, including the recurring ones.
- [ ] Send the thank-you, the feedback survey and the testimonial ask. Ops archives the Supered plan.
- [ ] Set up the monthly dashboard email for the monitoring period.

Done when The graduation gate is met. Health keeps its last value; it is not a completion status.

13 After the program

`6 months after the end · P9` Architect

- [ ] Monthly: the KPI snapshot email with 3 short notes from the Architect.
- [ ] Act on portal health alerts: deliverability drops, workflow errors, form submissions falling.
- [ ] Check-ins at month 3 and month 6. At month 5, present the paid options.
- [ ] A paid offer becomes a new deal. With no paid offer, set Current section to Completed at month 6.

Done when The customer is on a paid offer, or monitoring has ended cleanly.

Graduation gate

- [ ] Contracted scope is delivered, or explicitly waived with a recorded reason.
- [ ] Customer acceptance is captured where required.
- [ ] Training is complete, and the customer knows how to get support.
- [ ] Every progress measure has a final value from a real source and a continuing owner.
- [ ] Critical blockers are resolved or formally handed to an owner.
- [ ] Every open task and request is finished, transferred, or parked with the customer's agreement.
- [ ] The customer has agreed what happens next and received a short closeout recap.

Only then set Current section to Completed. Keep the row as history; a later onboarding gets a new row.

06 · REQUESTS

$250 per request, handled by urgency

The Request table is internal. Customers ask by email, Slack, in office hours or in Supered, and the Architect logs it the same day.

- One request = one deliverable that takes up to about 2 hours (one email, one form, one workflow change, one report).
- Bigger than that becomes a scoped quote, not a request.
- Anything in the customer's plan (Task Template) is never a request.

URGENCY	WHAT IT IS	RESPONSE AND TURNAROUND	PRICE
Critical	Something live is broken: forms not submitting, emails not sending, a workflow sending the wrong email, tracking down.	Reply within 4 business hours; fixed within 1 business day.	Free if it's in something we built; otherwise $250
High	Needed for a launch or deadline in the next 2 weeks.	Reply within 1 business day; done within 5 business days.	$250
Standard	A small new request with no hard deadline.	Reply within 1 business day; done within 10 business days.	$250
Not now	An idea or a bigger project for later.	Logged and reviewed at MBRs and the 'what's next' call.	Quoted when scoped

STATUS	MEANING
New	Logged, not yet triaged. Confirm owner, urgency, type and next step.
Quoted	Scope, price and date proposed. No chargeable work until the customer approves.
In progress	Approved and started. Keep the owner, due date and next update current.
Done	Verified and communicated, with customer validation where needed.
Parked	Deferred or declined, with the reason and a review date. Feeds the what's next call.

07 · STATUSES AND DATA RULES

When to change a status

TASK STATUS	WHEN
Not started	Default when the Task Generator copies the task in.
In progress	Someone has started it. Move it the day you start.
Waiting on client	Blocked on the customer: access, DNS, content or an answer. The Delay Flagger chases after 3 days.

TASK STATUS	WHEN
In review	Built and waiting for the customer's sign-off.
Done	The definition of done is met and checked. The Architect marks client-owned tasks Done once verified. Recurring tasks are marked Done at close-out.
Won't do	Doesn't apply to this customer, such as an optional measure they didn't buy or an Enterprise-only item for a Pro customer. Add a note saying why.

FIELD OR STATE	WHAT IT MEANS
Tasks created for	Lists the products whose tasks exist. It says nothing about whether they're finished.
Customer Task: Done	The definition of done is met and the evidence is recorded.
Request: Done	The result is verified and communicated to the customer.
Current section: Completed	The graduation gate is met and support has an owner. It is not a Health value.
Update: Draft / Reviewed / Sent	An agent wrote it / the Architect checked it / it went to the customer. Only weekly updates and KPI snapshots can be Sent.
Current section and Next due task	Portfolio summaries. The task rows are the truth.
Price	USD, default 250. The default is not a quote and not the customer's approval.

A normal week

WHEN	WHO	WHAT HAPPENS
Every day, 6:00 AM	**HubSpot Work**	Portfolio Sync updates Current section and Next due task.
Weekdays, 8:00 AM	**HubSpot Work**	Delay Flagger messages the Architect about overdue or stuck tasks.
Monday	**Architect**	Plans the week from My tasks and This week, and moves tasks to In progress.
Any day	**Customer**	Books office hours and sends requests.
Any day	**Architect**	Logs requests the day they arrive.
Once a week	**Phil + Architects**	Delivery review: Health board, Overdue view, Capacity report.
Thursday, 9:00 AM	**HubSpot Work**	Weekly Update Drafter writes each customer's draft.
Friday	**Architect**	Adds the numbers, sends the update, marks it Sent and sets Health.

Every working day

- [ ] Review due and overdue tasks; separate delays from Waiting on client.
- [ ] Every blocked item has an owner and a next action.
- [ ] Triage new requests.
- [ ] Review Health changes and delay flags.

Every week

- [ ] Send the Friday update and mark it Sent.
- [ ] Set Health from evidence.
- [ ] Check Current section and Next due task.
- [ ] Phil's delivery review.

Every month

- [ ] MBR: actuals vs baseline and target.
- [ ] Reconfirm scope, risks and measure owners.
- [ ] Near the end: prepare the what's next options.

Customer touchpoints

TOUCHPOINT	TIMING	CHANNEL	OWNER	CONTENT
Welcome email #1	Day 0	Email from Phil	Ops (automated)	Welcome, Supered Action Plan link, kickoff booking link, first to-dos (access + intake).
Welcome email #2	Day 2	Email	Ops (automated)	How we work: office hours, weekly updates, requests and urgency classes ($250), escalation path, AI use.
Access / intake reminders	Day 3–5 if incomplete	Email	Architect	Friendly reminder listing the exact missing items.

TOUCHPOINT	TIMING	CHANNEL	OWNER	CONTENT
Supered announcement	Day 2–3	Supered	Architect	How Supered works: Bases, announcements, documentation.
Kickoff (15 min)	Day 5–10	Video call	Architect	Intros, plan, missing items, office hours, MBRs.
Kickoff recap	Within 24h of kickoff	Email	Architect	Decisions, owners, dates, client to-dos.
Weekly update	Every Friday	Email	Architect (AI draft)	1) Work done and the strategic issue it moves 2) Numbers vs baseline 3) Issues found outside scope 4) Next week 5) Your to-dos.
Delivery announcement	Each delivery	Supered video	Architect	What was built, how to use it, why it matters.
Office hours	Weekly slots	Booking link	Architect	Questions, coaching, training practice.
MBR	Monthly (≈ Day 30 and 60)	Video call	Architect (Phil optional)	Progress vs baseline, numbers trend, issues and opportunities.
What's next	≈ 30 days before the end	Video call	Architect	Long-term vision, A/B next phase.
Final results review	Last week of the program	Video call	Architect	Before vs after, what we built, what's open.
KPI snapshot	Monthly for 6 months after	Scheduled dashboard email	Architect	Progress measures + 3 short notes.

09 · AUTOMATION YOU'LL WORK WITH

What HubSpot Work does for you, and what you still own

Agents only draft, fill fields or flag. None of them sends anything to a customer or changes a deal. Every draft waits for a person.

AUTOMATION	WHAT IT DOES	WHEN IT RUNS	WHAT YOU DO
Task Generator	Copies the Core library plus one library per product into Customer Task, fills the dates and assigns the Architect's tasks.	When Ops ticks Create tasks	Ops checks the task count.
Handoff Brief	Writes a one-page brief from the deal for the Architect and Phil.	When a customer's tasks are first created	Phil and the Architect review it before the handoff call.
Weekly Update Drafter	Drafts each customer's Friday update.	Thursdays, 9:00 AM Bogotá	The Architect checks it, adds numbers, sends it and marks it Sent.
Delay Flagger	Flags overdue and stuck tasks; sets Health to At risk at 3 or more overdue; alerts Phil when Health drops.	Weekdays, 8:00 AM Bogotá	The Architect confirms the impact and owns the recovery plan.
Request Triage	Suggests the urgency, price and due date for each new request, and fills its Owner.	When a request is logged	The Architect confirms it with the customer.
Portfolio Sync	Keeps each customer's Current section and Next due task up to date.	Daily, 6:00 AM Bogotá	If a summary looks wrong, fix the task data, not the summary.
What's Next Prep	Drafts Option A and Option B for the next phase.	35 days before the Target end date	Phil and the Architect review it before the call.
KPI Snapshot Drafter	Drafts the monthly KPI notes during free monitoring.	1st of the month, 9:00 AM Bogotá	The Architect adds the numbers and sends it.
Data rules	Re-dates a customer's tasks when Start date or Program length changes, and only lets weekly updates and KPI snapshots be marked Sent.	On every change	Nothing to do.

10 · WHEN THINGS DON'T GO TO PLAN

Exceptions

SITUATION	WHAT TO DO
The customer is slow with access or the intake	Task goes to Waiting on client. Chase on Day 3. On Day 7, escalate to Phil using the escalation path and set Health to At risk.
A pre-sale item is missing at handoff	The Architect flags it on the P0 task. Phil fixes it within 24 hours.

SITUATION	WHAT TO DO
The customer wants to pause	Set Health to Off track with a note. If the pause is longer than 2 weeks, move the Start date forward by the pause length. The Task Generator re-dates every task.
The Architect changes	Change the Architect on the Customers row. The Task Generator moves the open Architect tasks to the new person.
The program length changes	Change Program length (60, 75 or 90). Every due date recalculates.
A due date lands on a weekend or holiday	Dates are calendar days, so treat it as the next business day.
Something live breaks	Log it as a Critical request. Fix it within 1 business day. It's free if it's in something we built.
The customer wants to buy more mid-program	Log a request. It becomes Quoted, then a deal. This program's tasks don't change.
The customer buys another hub mid-program	Add it to Products purchased and tick Create tasks. The Task Generator adds only that hub's tasks, dated from that day. Core tasks aren't duplicated.
Agreement or approval is missing	Keep the engagement out of active delivery until a start is authorized. Record the gap, an owner and the next action.
A draft contains a wrong or unsupported claim	Don't share it. Fix the source record, revise the draft, and have the Architect confirm the evidence.
The program ends with open items	Agree item by item: finish, hand to support, or park. Don't set Completed until each has an owner.

11 · AFTER THE PROGRAM

6 months free, then a paid next step

Monitoring starts the day the program ends. The Architect runs every check-in and presents the paid options at month 5.

OFFER	PRICE	WHAT'S INCLUDED
KPI monitoring (6 months)	Free	Monthly KPI snapshot with Architect notes; portal health alerts; check-in calls at month 3 and month 6; requests still available at $250 each.
Team support	$1,670/mo (Monthly Plan – Standard, one task at a time)	Same Architect, ongoing requests one at a time, weekly office hours.
Build internal capacity	Quoted per customer	Coach their in-house marketer or admin: monthly training plan, admin office hours, HubSpot certification path, help hiring a marketing ops role.
One initiative a month	Quoted per customer	One scoped project per month from the 'not now' list (a new nurture, a campaign, a report pack, another tool migration).

WHEN	WHAT HAPPENS
Monthly	KPI snapshot email: the progress-measure dashboard with 3 short notes from the Architect.
Any time	Portal health alerts: deliverability drops, workflow errors, form submissions falling. Tell the customer when one fires.
Month 3	30-minute check-in: numbers, what's working, what's next.
Month 5	Paid offer conversation: team support, building internal capacity, or one initiative a month.
Month 6	Last check-in. A paid offer becomes a new deal; otherwise set Current section to Completed.

APPENDIX A

Task library

Every customer gets the Core tasks once, plus the module for each hub bought. Days are for a 90-day program. Module colors: Core Marketing Sales Service

P0 · Handoff checklist Day -30–0

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
0.01	**Research brief from company URL** Website URL on the deal; research brief attached as a note before the Fit call.	Core	Phil	Before Day 0	
0.02	**FigJam canvas after Fit call** Covers strategic motivation, tactical outcomes, progress measures and fee range. Link saved on the deal.	Core	Phil	Before Day 0	
0.03	**From→To statement captured** One sentence: from where they are today to where they want to be. Every weekly update ties back to it.	Core	Phil	Before Day 0	
0.04	**Tech stack & team capacity survey** Client gave HubSpot access and finished the survey: tools beyond HubSpot, internal processes and cadences, current KPIs.	Core	Client POC	Before Day 0	Yes
0.05	**Products and quote on the deal** Pricing calculator used, line items added, quote created. Each hub bought is Pro or Enterprise.	Core	Phil	Before Day 0	
0.06	**Progress measures picked** The standard progress measures for each hub bought (Progress Measures tab), plus any optional ones. Baselines noted if known.	Core	Phil	Before Day 0	
0.07	**POC and supporters identified** Contacts on the deal with labels (POC, Supporter, Billing, Decision maker). POC gets the weekly email.	Core	Phil	Before Day 0	Yes
0.08	**Agreement signed** Includes AI terms, escalation path, how progress is measured, POC and supporters, strategic job → tactical outcomes → progress measures, and request handling ($250 per request, urgency classes).	Core	Client POC	Before Day 0	Yes

P1 · Close & welcome Day 0–3

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
1.01	**Pick the Architect** Phil checks the Capacity report (active customers per Architect) and picks the Architect.	Core	Phil	Day 0–1	

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
1.02	**Add the customer in HubSpot Work** Add a Customers row: Customer, Company, Deal, Architect, Program length, Start date (the payment date), Products purchased, hub tiers, From→To goal, FigJam and Supered links. Tick Create tasks and check the Task Generator filled Tasks created for.	Core	Ops	Day 0–1	
1.03	**Welcome email #1: welcome + Action Plan** Sent from Phil on Day 0: Supered Action Plan link, kickoff booking link, first to-dos (grant HubSpot access, fill the intake form).	Core	Ops	Day 0	Yes
1.04	**Build the Supered Action Plan** Duplicate the Action Plan template for the products bought; add the agreement, FigJam, client to-dos and access checklist.	Core	Ops	Day 0–1	Yes
1.05	**Phil ↔ Architect handoff (30 min)** Walk through FigJam, customer context, products, the From→To goal, progress measures and KPIs, schedule. Architect checks the Handoff checklist section. Strategy lead moves to the Architect after this call.	Core	Phil	Day 1–3	
1.06	**Set up progress measures** Add the customer's progress measures to their Customers row (name '<Client> 1.1 Visitor to Lead' etc.) with baseline, target and schedule.	Core	Architect	Day 1–3	
1.07	**Office hours booking link** Architect's HubSpot meetings link (office-hours type) added to the Supered plan.	Core	Architect	Day 1–2	Yes
1.08	**Welcome email #2: how we work** Day 2: office hours, Friday updates, how to send a request and the urgency classes, escalation path, how we use AI.	Core	Ops	Day 2	Yes
1.09	**Kickoff booked** Client books the 15-minute kickoff from welcome email #1. Chase on Day 3 if not booked.	Core	Client POC	Day 0–5	Yes

P2 · Access & intake Day 1–7

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
2.01	**HubSpot access granted** Partner access or a Super Admin user for the Architect. Confirm Pro or Enterprise per hub.	Core	Client POC	Day 1–3	Yes
2.02	**Intake form submitted** Short form with only what pre-sale didn't capture (Intake Form tab).	Core	Client POC	Day 1–5	Yes

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
2.03	**Access to connected systems** DNS/IT contact, website CMS, GA4/GTM, ad and social accounts, and every old tool we migrate from (email tool, CRM, help desk).	Core	Client POC	Day 1–7	Yes
2.04	**Brand & content assets shared** Brand guide, logos, fonts, colors, email templates, key content, lists to import.	Core	Client POC	Day 1–7	Yes
2.05	**Supered announcement to POC** Short video: how Supered works (Bases, announcements, documentation) and where updates show up.	Core	Architect	Day 2–3	Yes
2.06	**Portal audit** Data health, email health, existing assets, tracking, workflows, properties, old tool inventory. 1-page summary for kickoff.	Core	Architect	Day 3–7	
2.07	**Baseline numbers** Record the 'before' number for each progress measure.	Core	Architect	Day 5–7	

P3 · Kickoff Day 5–10

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
3.01	**Kickoff agenda** Plan summary, missing items, decisions needed. Drafted from intake + audit.	Core	Architect	Day 5–7	
3.02	**Kickoff session (15 min)** Architect & team intro; confirm the goal and plan; walk through missing items; explain office hours, Friday updates, MBRs and how to send requests.	Core	Architect	Day 5–10	Yes
3.03	**Book MBRs and the 'what's next' call** MBR #1 ≈ Day 30, MBR #2 ≈ Day 60, 'what's next' ≈ Day 60–65, final results review ≈ Day 85 (scaled to program length).	Core	Architect	Day 5–10	Yes
3.04	**Kickoff recap within 24h** Decisions, owners, dates, client to-dos. Supered plan updated.	Core	Architect	Day 6–11	Yes

P4 · Foundations Day 7–30

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
4.01	**Account, users & security** Users, permission sets, 2FA; Enterprise extras where bought. Subtasks: Users & permission sets; Require 2FA; Single sign-on (SSO) (Ent); Brands / business units (Ent); Sandbox account (Ent)	Core	Architect	Day 7–12	

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
4.05	**Data model** Property audit, lifecycle stage definitions, lead status, marketing-contact rules. Subtasks: Property audit; Lifecycle stages & lead status; Marketing contact rules; Custom behavioral events (Ent)	Core	Architect	Day 10–21	
4.07	**Data import & cleanup** Import contacts and companies (including migrated data, with consent mapped and unsubscribes suppressed), dedupe, associations, marketing contacts. Subtasks: Import contacts & companies; Data hygiene workflows	Core	Architect	Day 14–25	
4.09	**Integrations** Every integration the intake lists: GA4, ad and social accounts, webinar tool, Slack, CRM sync if their CRM isn't HubSpot. Mark the ones this customer doesn't need as not applicable. Subtasks: GA4; Ad accounts; Social accounts; Webinar, Slack, other apps; CRM sync (if CRM isn't HubSpot)	Core	Architect	Day 14–28	
4.10	**Baseline dashboard** One report per progress measure, showing baseline vs now. Used in every weekly update. Subtasks: Baseline dashboard	Core	Architect	Day 18–28	Yes
4.11	**Foundation QA** Test the main flow end to end for each hub bought (Marketing: visit → form → contact → email; Sales: lead → owner → deal; Service: email → ticket → reply). Subtasks: End-to-end test	Core	Architect	Day 25–30	
4.12	**Supered video: foundations done** What changed for the customer and why it matters.	Core	Architect	Day 28–30	Yes
MH-4.02	**Tracking & consent** Tracking code on every domain, internal traffic excluded, cookie banner set. Subtasks: Tracking code on every domain; Exclude internal traffic; Cookie consent banner	Marketing	Architect	Day 7–14	
MH-4.03	**Domains & email authentication** Content domain connected; sending domain authenticated (SPF, DKIM, DMARC) with the client's DNS contact. Subtasks: Connect content domain; Email sending domain authentication	Marketing	Architect	Day 7–18	
MH-4.04	**Email foundations** Subscription types, footer and address, brand kit, email templates, default sender. Subtasks: Subscription types; Footer, address, default sender; Brand kit & email templates	Marketing	Architect	Day 10–18	

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
MH-4.06	**Migration plan & export** Inventory and export from the old tool: lists, consent, unsubscribes and bounces, templates, active automations. Subtasks: Old tool inventory; Export lists with consent	Marketing	Architect	Day 8–16	
MH-4.08	**Website connection** HubSpot forms, CTAs, chat and meetings on the current website; landing page and blog templates. Subtasks: HubSpot forms on the site; CTAs, chat & meetings on the site; Landing page & blog templates	Marketing	Architect	Day 14–28	
SH-4.01	**Sales users, seats & inboxes** Sales Hub seats assigned, teams and permission sets set, every rep's inbox and calendar connected, email tracking and logging on. Subtasks: Assign Sales Hub seats; Teams & permission sets; Connect rep inboxes & calendars	Sales	Architect	Day 7–12	
SH-4.02	**Deal pipelines & stages** One pipeline per sales motion. Each stage has exit criteria, a probability and required properties, agreed with the sales lead. Subtasks: One pipeline per sales motion; Stage exit criteria & probabilities; Required properties per stage	Sales	Architect	Day 8–18	Yes
SH-4.03	**Lead management & assignment** Lead status and lifecycle definitions agreed with marketing, assignment rules (rotation or territory), follow-up SLA. Subtasks: Lead status & lifecycle definitions; Assignment rules	Sales	Architect	Day 10–21	Yes
SH-4.04	**Products, quotes & e-signature** Product library, quote templates, e-signature, payments if they use them. Subtasks: Product library; Quote templates & e-signature	Sales	Architect	Day 14–25	
SH-4.05	**CRM migration** Companies, contacts, open deals, owners and activity history moved from the old CRM or spreadsheets, using a field map the client approved. Subtasks: Field map approved by the client; Import companies, contacts & open deals; Import activity history	Sales	Architect	Day 10–25	Yes
SH-4.06	**Sales integrations** Calling, Zoom or Teams, LinkedIn Sales Navigator, accounting or ERP if needed. Subtasks: Calling and video meetings; LinkedIn Sales Navigator	Sales	Architect	Day 14–28	

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
SV-4.01	**Service users, seats & help desk** Service Hub seats, teams and permission sets, the help desk workspace and business hours. Subtasks: Assign Service Hub seats; Help desk workspace & business hours	Service	Architect	Day 7–12	
SV-4.02	**Support channels** Support email, chat, forms and calling connected to the help desk, plus WhatsApp or Messenger if used. Subtasks: Support email connected; Chat & support form	Service	Architect	Day 8–18	Yes
SV-4.03	**Ticket pipelines & routing** Ticket pipelines and stages, priority and category properties, required fields, routing rules. Subtasks: Ticket pipelines & stages; Priority, category & routing rules	Service	Architect	Day 10–21	Yes
SV-4.04	**Help desk migration** Open tickets, ticket history, knowledge base articles and saved replies moved from the old help desk. Subtasks: Import open tickets & history; Import knowledge base articles	Service	Architect	Day 10–25	Yes
SV-4.05	**SLAs & escalation** First-response and time-to-close SLAs by priority, escalation rules, business hours. Subtasks: SLA rules by priority	Service	Architect	Day 14–25	Yes

P5 · Build & launch Day 21–75

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
5.11	**Client sign-off per progress measure** Client approves each build before it goes live.	Core	Client POC	Day 35–75	Yes
5.12	**Supered video per delivery** What was built, how to use it, why it matters.	Core	Architect	Day 35–75 After each delivery	Yes
MH-5.01	**Build 1.1 Visitor → Lead** Forms, CTAs, landing and thank-you pages live on the right pages. Measure: visit-to-contact rate. Subtasks: Forms, CTAs, landing & thank-you pages	Marketing	Architect	Day 21–40	
MH-5.02	**Build 1.2 Lead → MQL** Segments, nurture emails and workflows, lead scoring, lifecycle automation. Client approves copy. Measure: lead-to-MQL rate. Subtasks: Core segments; Nurture workflows & emails; Lead scoring	Marketing	Architect	Day 30–55	Yes

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
MH-5.03	**Build 1.3 MQL → Meeting** MQL definition agreed with sales, owner assignment, notifications, follow-up SLA, meetings link in nurture. Measure: MQL-to-meeting rate. Subtasks: MQL handoff	Marketing	Architect	Day 35–60	Yes
MH-5.04	**Build 1.4 Subscriber → Engaged (if bought)** Newsletter or content program, subscription preferences, re-engagement and sunset flows. Measure: email click rate, engaged contacts. Subtasks: Re-engagement & sunset flows	Marketing	Architect	Day 35–60	
MH-5.05	**Build 1.0 Stranger → Visitor (if bought)** Campaigns and UTMs, ad audiences and conversion events, social publishing, SEO recommendations. Measure: sessions by source. Subtasks: Campaigns, UTMs & ad audiences	Marketing	Architect	Day 30–60	
MH-5.06	**Migration: rebuild and switch off old tool** Rebuild templates and active automations from the old tool, send in parallel once, then switch the old tool off. Subtasks: Rebuild templates & automations; Parallel send, then switch off the old tool	Marketing	Architect	Day 25–50	Yes
MH-5.07	**Website: landing pages & blog** Migrate landing pages and blog posts within the agreed limit; redirects set. Subtasks: Migrate landing pages & blog	Marketing	Architect	Day 30–60	Yes
MH-5.08	**First campaign live** Campaign with UTMs and assets, launched with the client.	Marketing	Architect	Day 40–65	Yes
MH-5.09	**Performance reporting** Marketing performance dashboard and funnel by progress measure; revenue attribution on Enterprise. Subtasks: Marketing performance dashboard; Revenue attribution reports (Ent)	Marketing	Architect	Day 45–70	Yes
MH-5.10	**AI / Breeze setup** Brand voice and content tools, only within the AI terms in the agreement. Subtasks: Breeze / AI settings	Marketing	Architect	Day 45–70	
SH-5.01	**Build 2.1 Lead → Contacted** Lead rotation, task queues, a first-touch sequence and new-lead notifications. Measure: share of leads contacted within 24 hours. Subtasks: Lead rotation & task queues; First-touch sequence	Sales	Architect	Day 21–40	Yes

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
SH-5.02	**Build 2.2 Meeting → Qualified deal** Meetings links per rep, qualification properties, deal creation from meetings, call playbooks. Measure: meeting-to-deal rate. Subtasks: Qualification properties & playbooks	Sales	Architect	Day 28–50	Yes
SH-5.03	**Build 3.1 Deal → Proposal sent (if bought)** Stage-based tasks and reminders, deal workflows, quote steps in the pipeline. Measure: stage conversion and days in stage.	Sales	Architect	Day 35–55	
SH-5.04	**Build 3.2 Proposal → Closed won** Quotes and e-signature in the flow, a closed-won handoff workflow, closed-lost reasons. Measure: win rate and sales cycle length. Subtasks: Closed-won handoff workflow; Closed-lost reasons	Sales	Architect	Day 35–60	Yes
SH-5.05	**Templates, snippets & sequences** Email templates, snippets and sequences per persona and stage, approved by the sales lead.	Sales	Architect	Day 30–55	Yes
SH-5.06	**Sales reporting & forecasting** Pipeline dashboard, forecast, goals or quotas, rep activity report. Subtasks: Pipeline dashboard & forecast	Sales	Architect	Day 45–70	Yes
SH-5.07	**AI / Breeze for sales** Prospecting and deal tools, only within the AI terms in the agreement.	Sales	Architect	Day 45–70	
SV-5.01	**Build 4.1 Ticket → Resolved** Routing, SLA alerts, ticket automation, snippets and templates, escalation workflows. Measure: time to first response and time to close. Subtasks: Ticket automation & snippets	Service	Architect	Day 21–45	Yes
SV-5.02	**Build 4.2 Question → Self-served** Knowledge base structure and the top 20 articles, customer portal if bought, AI chat within the AI terms. Measure: knowledge base views vs new tickets. Subtasks: Structure & top 20 articles	Service	Architect	Day 30–60	Yes
SV-5.03	**Build 4.3 Customer → Renewed (if bought)** CSAT or NPS surveys, customer success workspace, health scores, renewal reminders. Measure: survey response, health score and renewal rate. Subtasks: CSAT or NPS surveys; Customer success workspace & health scores (Ent)	Service	Architect	Day 35–65	Yes

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
SV-5.04	**Service reporting** Help desk dashboard, SLA report, agent performance, CSAT trend. Subtasks: Help desk & SLA dashboard	Service	Architect	Day 45–70	Yes
SV-5.05	**AI / Breeze for service** Customer agent and help desk AI tools, only within the AI terms in the agreement.	Service	Architect	Day 45–70	

P6 · Training & adoption Day 14–85

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
6.01	**Confirm training plan** Who needs which modules (Training tab), from the intake.	Core	Architect	Day 10–14	Yes
6.03	**Adoption check #1** Logins, emails sent, workflows active, dashboards viewed. Flag low adoption in the weekly update.	Core	Architect	Day 45	
6.04	**Admin handbook (Supered Base)** How the portal is set up: naming, properties, workflows, who owns what.	Core	Architect	Day 60–85	Yes
6.05	**Adoption check #2** Same check before the final results review.	Core	Architect	Day 75	
MH-6.02	**Deliver Marketing Hub training** Modules T1–T9 as Supered videos + practice in office hours, timed to when each feature ships.	Marketing	Architect	Day 14–85	Yes
SH-6.02	**Deliver Sales Hub training** Modules S1–S5 as Supered videos + practice in office hours, timed to when each feature ships.	Sales	Architect	Day 14–85	Yes
SV-6.02	**Deliver Service Hub training** Modules V1–V5 as Supered videos + practice in office hours, timed to when each feature ships.	Service	Architect	Day 14–85	Yes

P7 · Run cadence Day 7–90

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
7.01	**Office hours** Bookable slots for questions, coaching and training practice.	Core	Architect	Day 7–90 Weekly	Yes
7.02	**Weekly update** Drafted with AI, reviewed and sent by the Architect: work done and the strategic issue it moves, numbers vs baseline, issues found outside scope, next week, client to-dos.	Core	Architect	Day 7–90 Weekly (Friday)	Yes

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
7.03	**Handle requests by urgency** Every request gets logged with an urgency class and handled in that time ($250 per request; see Request Classes).	Core	Architect	Day 7–90 As they come in	Yes
7.04	**Log issues and 'not now' ideas** Out-of-scope issues and client ideas go to the Request table as 'Not now', to sell later.	Core	Architect	Day 7–90 As they come in	
7.05	**Health check** Set Health (On track / At risk / Off track) and blockers. Escalate per the escalation path.	Core	Architect	Day 7–90 Weekly	
7.06	**Monthly Business Review** Progress vs baseline, numbers trend, issues and opportunities. Architect leads; Phil optional.	Core	Architect	Day 30–60 Monthly	Yes
7.07	**Internal delivery review** Phil + Architects: at-risk customers, capacity, blockers.	Core	Phil	Day 7–90 Weekly	

P8 · What's next Day 60–90

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
8.01	**Prep next-phase options** Results so far, issues found and 'not now' list → Option A and Option B. Phil reviews before the call.	Core	Architect	Day 55–60	
8.02	**'What's next' call** Architect explains the long-term vision and the next phase as an A/B choice.	Core	Architect	Day 60–65	Yes
8.03	**Next-phase proposal** New deal in the Sales Pipeline for the chosen offer.	Core	Architect	Day 62–70	Yes
8.04	**Final results review** Before vs after for every progress measure, what we built, what's still open.	Core	Architect	Day 80–88	Yes
8.05	**Close the program** Supered plan archived, project marked Completed, feedback and testimonial asked for.	Core	Architect	Day 85–90	Yes

P9 · After the program Day 90–270

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
9.01	**Monthly KPI snapshot** Progress-measure dashboard emailed with 3 short notes from the Architect.	Core	Architect	Day 90–270 Monthly × 6	Yes

ID	TASK AND DEFINITION OF DONE	MODULE	OWNER	WHEN	CLIENT
9.02	**Portal health alerts** Watch for deliverability drops, workflow errors, form submissions down 30%+. Tell the client when one fires.	Core	Architect	Day 90–270 Ongoing	Yes
9.03	**Check-in call: month 3** 30 minutes: numbers, what's working, what's next.	Core	Architect	Day 180	Yes
9.04	**Paid offer conversation: month 5** Present team support, internal capacity and one-initiative-a-month before monitoring ends.	Core	Architect	Day 240	Yes
9.05	**Check-in call: month 6** Final monitoring check-in; confirm the paid offer or close monitoring.	Core	Architect	Day 270	Yes

APPENDIX B

Progress measures

Name each one after the customer, e.g. "<Client> 1.1 Visitor to Lead". 1.x is Marketing, 2.x and 3.x are Sales, 4.x is Service. "Every" measures go into every program for that hub; the others only when bought.

ID	PROGRESS MEASURE	WHEN	WHAT IT MEASURES	HUBSPOT REPORT	BUILT BY
0.1	**Database → Marketable database**	Every Marketing Hub customer	% of contacts with lifecycle stage and original source set; marketable contacts; bounce rate under 2%.	Contacts by lifecycle stage; email health	4.05, MH-4.06, 4.07
1.1	**Visitor → Lead**	Every Marketing Hub customer	Visit-to-contact conversion rate; new contacts from forms per month.	Sessions vs new contacts by source	MH-5.01, MH-4.08
1.2	**Lead → MQL**	Every Marketing Hub customer	Lead-to-MQL rate; MQLs per month.	Lifecycle stage funnel	MH-5.02
1.3	**MQL → Meeting**	Every Marketing Hub customer	MQL-to-meeting rate; time to first sales touch.	Funnel + meetings booked by source	MH-5.03
1.0	**Stranger → Visitor**	When ads, SEO or content is bought	Sessions per month by source.	Traffic analytics by source	MH-5.05
1.4	**Subscriber → Engaged**	When email programs are bought	Email click rate; contacts engaged in the last 90 days.	Email performance; engagement segment size	MH-5.04
2.1	**Lead → Contacted**	Every Sales Hub customer	Share of leads contacted within 24 hours; time to first touch.	Lead response time; contacts by lead status	SH-5.01
2.2	**Meeting → Qualified deal**	Every Sales Hub customer	Meeting-to-deal rate.	Meetings booked vs deals created	SH-5.02
3.1	**Deal → Proposal sent**	When pipeline automation is bought	Stage conversion; days in stage.	Deal stage funnel	SH-5.03
3.2	**Proposal → Closed won**	Every Sales Hub customer	Win rate; sales cycle length.	Deals won vs lost; cycle length	SH-5.04
4.1	**Ticket → Resolved**	Every Service Hub customer	Time to first response; time to close; SLA hit rate.	Help desk and SLA reports	SV-5.01
4.2	**Question → Self-served**	Every Service Hub customer	Knowledge base views vs new tickets.	Knowledge base and ticket volume	SV-5.02

ID	PROGRESS MEASURE	WHEN	WHAT IT MEASURES	HUBSPOT REPORT	BUILT BY
4.3	**Customer → Renewed**	When customer success is bought	Survey response, health score, renewal rate.	Feedback surveys; customer success workspace	SV-5.03

APPENDIX C

Training modules

MODULE	AUDIENCE	CONTENT	FORMAT	WHEN	LENGTH
T1 · HubSpot basics	All client users	Navigation, records, notifications, where to find help.	Supered tour + video	After access (≈ Day 7)	10 min
T2 · Contacts & segments	Marketing team	Contact records, properties, segments, data hygiene habits.	Video + office hours practice	After data import (≈ Day 25)	20 min
T3 · Email marketing	Marketing team	Build, test, send and analyze emails with your templates.	Video + live build in office hours	After email foundations (≈ Day 20)	25 min
T4 · Forms, landing pages & CTAs	Marketing team	Create and edit lead capture assets.	Video	After 1.1 ships (≈ Day 40)	20 min
T5 · Workflows & nurture	HubSpot admin(s)	Read, edit and safely clone workflows.	Live session	After 1.2 ships (≈ Day 55)	30 min
T6 · Campaigns, ads & social	Marketing team	Campaigns, UTMs, ads and social reporting.	Video	After first campaign (≈ Day 65)	20 min
T7 · Reporting & dashboards	Marketing lead + leadership	Read the progress-measure dashboard; build a report.	Live at MBR #2	≈ Day 60	20 min
T8 · Lead handoff	Marketing + sales	MQL definition, notifications, follow-up SLA.	Live session	After 1.3 ships (≈ Day 60)	20 min
T9 · Admin handbook	HubSpot admin(s)	How your portal is built and how to maintain it.	Supered Base	≈ Day 85	Self-serve
S1 · CRM every day	Sales reps	Records, tasks, inbox, logging calls and emails.	Video + office hours practice	After inboxes connect (≈ Day 14)	20 min
S2 · Pipeline & deals	Sales reps + manager	Moving deals, stage rules, required fields.	Live session	After pipelines (≈ Day 20)	25 min
S3 · Sequences & templates	Sales reps	Enroll, personalize and track sequences.	Video	After 2.1 ships (≈ Day 40)	20 min

MODULE	AUDIENCE	CONTENT	FORMAT	WHEN	LENGTH
S4 · Quotes & closing	Sales reps	Build a quote, send it for signature, close the deal.	Video	After 3.2 ships (≈ Day 60)	20 min
S5 · Forecast & reports	Sales manager	Forecast, goals, pipeline and activity reports.	Live at MBR #2	≈ Day 60	20 min
V1 · Help desk basics	Support team	Working tickets, snippets, internal notes.	Video + office hours practice	After channels connect (≈ Day 18)	20 min
V2 · SLAs & routing	Support lead	How routing and SLAs work, and how to change them.	Live session	After SLAs (≈ Day 25)	20 min
V3 · Knowledge base	Support team	Write, publish and update articles.	Video	After 4.2 ships (≈ Day 60)	20 min
V4 · Feedback & customer success	Support lead + CS	Read surveys and health scores, and follow up.	Video	After 4.3 ships (≈ Day 65)	20 min
V5 · Service reports	Support lead	Help desk, SLA and CSAT reports.	Live at MBR #2	≈ Day 60	20 min

APPENDIX D

Intake questions

Only what pre-sale didn't capture. Items marked as pre-filled are shown to the customer to confirm.

SECTION	QUESTION	FIELD	REQUIRED	PRE-FILLED?	WHY WE ASK
Contacts	Main point of contact (name, email, role)	Text	Yes	Yes (confirm)	One owner for approvals and to-dos.
Contacts	Supporters who should get updates or training	Multi-line text	Yes	Partly	Training plan and weekly update recipients.
Contacts	Who controls your DNS / IT?	Text	Yes	No	Email authentication and domain connection.
Contacts	Preferred channel for quick questions	Dropdown: Email / Slack Connect / Teams	Yes	No	How office-hours follow-ups happen.
Contacts	Time zone and best days for office hours	Text	No	No	Office hours slots.
Goals	In one sentence: from where to where? (pre-filled from the sale)	Multi-line text	Yes	Yes (confirm)	The goal every update ties back to.
Goals	Top 3 results you want by the end of the program	Multi-line text	Yes	Partly	Prioritizes the build.
Goals	How do you report marketing results today, and to whom?	Multi-line text	Yes	Partly	Shapes dashboards and MBRs.
Goals	Current numbers: monthly sessions, leads, MQLs, meetings, customers	Number fields	No	Partly	Baselines for progress measures.
Audience	Who are your buyers? (personas / segments)	Multi-line text	Yes	No	Segments and nurture.
Audience	How do you define a marketing-qualified lead today?	Multi-line text	Yes	No	Progress measures 1.2 and 1.3.

SECTION	QUESTION	FIELD	REQUIRED	PRE-FILLED?	WHY WE ASK
Marketing today	Channels you use	Checkboxes: SEO, Paid search, Paid social, Organic social, Email, Events/Webinars, Partners, Outbound	Yes	Partly	Integrations and optional progress measures.
Marketing today	Campaigns or launches planned in the next 90 days	Multi-line text	No	No	Pick the first campaign.
Marketing today	Who on your team will run HubSpot, and hours per week	Text	Yes	Partly	Training scope and a realistic timeline.
Marketing today	Other agencies or freelancers involved	Text	No	No	Avoid overlap.
Approvals	Who approves emails/pages before they go live, and how fast?	Text	Yes	No	Sign-off turnaround in the plan.
Tech	Marketing Hub tier	Dropdown: Professional / Enterprise	Yes	Yes (confirm)	Which setup items apply.
Tech	Website platform and who can edit it	Dropdown + text	Yes	Partly	Website connection.
Tech	Email domain you send from	Text	Yes	No	Email authentication.
Migration	Which email/marketing tool are you moving from, and what's active in it today?	Text + multi-line text	Yes	Partly	Migration plan.
Migration	Where do your contacts live today and roughly how many?	Text + number	Yes	No	Import scope and marketing contacts.
Website	Landing pages and blog posts to bring over (links or count)	Multi-line text	No	No	Website scope within the limit.
Tech	Other tools to connect (CRM, ads, webinar, chat, analytics)	Multi-line text	Yes	Partly	Integrations.
Compliance	Regions you market to and consent rules you follow	Checkboxes: US, Canada (CASL), EU/UK (GDPR), Other	Yes	No	Subscription types, consent, cookie banner.

SECTION	QUESTION	FIELD	REQUIRED	PRE-FILLED?	WHY WE ASK
Compliance	Industry regulations (e.g. HIPAA, financial)	Text	No	No	Data handling limits.
Brand	Upload brand guide, logos, fonts, email templates	File upload	Yes	No	Brand kit and templates.
Access	Checklist: HubSpot access, website admin, GA4/GTM, ad accounts, social accounts, old tool login	Checkboxes	Yes	Partly	One list so access isn't chased for weeks.
Sales Hub	Which CRM or spreadsheet are you moving from, and how many open deals?	Text + number	If Sales Hub	Partly	CRM migration scope.
Sales Hub	Your sales stages today, and what has to be true to move a deal forward	Multi-line text	If Sales Hub	No	Pipeline design.
Sales Hub	How many reps, and how leads are assigned today	Text	If Sales Hub	No	Seats and lead rotation.
Service Hub	Which help desk are you moving from, and which channels do customers use (email, chat, phone)?	Multi-line text	If Service Hub	Partly	Channels and migration.
Service Hub	Response and resolution times you promise customers today	Text	If Service Hub	No	SLAs.
Service Hub	Do you run surveys (CSAT, NPS) or track renewals?	Text	If Service Hub	No	Progress measure 4.3.

APPENDIX E

Technical setup checklist

Each item is a subtask of the task in the last column. "Ent only" items apply to Enterprise customers.

AREA	ITEM	DETAILS	TIER	TASK
Account	Users & permission sets	Invite client users, set permissions by role, teams if needed.	Pro & Ent	4.01
Account	Require 2FA	For every user.	Pro & Ent	4.01
Account	Single sign-on (SSO)	If the client uses an identity provider.	Ent only	4.01
Account	Brands / business units	If they market more than one brand.	Ent only	4.01
Account	Sandbox account	Test workflows and changes before production.	Ent only	4.01
Tracking	Tracking code on every domain	CMS plugin or GTM. Verify with a test visit.	Pro & Ent	MH-4.02
Tracking	Exclude internal traffic	Client and RevGravy IPs/domains.	Pro & Ent	MH-4.02
Tracking	Cookie consent banner	Per the regions in the intake.	Pro & Ent	MH-4.02
Domains	Connect content domain	Landing pages / blog subdomain (e.g. go.client.com).	Pro & Ent	MH-4.03
Domains	Email sending domain authentication	SPF, DKIM, DMARC added by the client's DNS contact; verified in HubSpot.	Pro & Ent	MH-4.03
Email	Subscription types	Per content type; mapped to consent rules.	Pro & Ent	MH-4.04
Email	Footer, address, default sender	Compliant footer, real sender name.	Pro & Ent	MH-4.04
Email	Brand kit & email templates	Logo, colors, fonts; 2–3 reusable templates.	Pro & Ent	MH-4.04
Data	Property audit	Remove unused, add what the progress measures need. Naming convention documented.	Pro & Ent	4.05
Data	Lifecycle stages & lead status	Definitions agreed with the client; automation set.	Pro & Ent	4.05

AREA	ITEM	DETAILS	TIER	TASK
Data	Marketing contact rules	Who is a marketing contact; keeps billing under control.	Pro & Ent	4.05
Data	Custom behavioral events	Track key product or site actions.	Ent only	4.05
Migration	Old tool inventory	Lists, segments, templates, active automations, integrations.	Pro & Ent	MH-4.06
Migration	Export lists with consent	Including unsubscribes and hard bounces to suppress.	Pro & Ent	MH-4.06
Data	Import contacts & companies	Mapped import, consent mapped, unsubscribes suppressed, dedupe, associations.	Pro & Ent	4.07
Data	Data hygiene workflows	Formatting, required fields, duplicates.	Pro & Ent	4.07
Website	HubSpot forms on the site	Replace or collect existing site forms.	Pro & Ent	MH-4.08
Website	CTAs, chat & meetings on the site	Placed on the pages that matter.	Pro & Ent	MH-4.08
Website	Landing page & blog templates	Matching the brand kit.	Pro & Ent	MH-4.08
Integrations	GA4	Connected for reporting.	Pro & Ent	4.09
Integrations	Ad accounts	Google, Meta, LinkedIn with conversion events.	Pro & Ent	4.09
Integrations	Social accounts	Connected for publishing and reporting.	Pro & Ent	4.09
Integrations	Webinar, Slack, other apps	As listed in the intake.	Pro & Ent	4.09
Integrations	CRM sync (if CRM isn't HubSpot)	Field mapping, sync rules, lifecycle alignment.	Pro & Ent	4.09
Reporting	Baseline dashboard	One report per progress measure; baseline vs now.	Pro & Ent	4.10
QA	End-to-end test	Visit → form → contact → workflow → email → notification.	Pro & Ent	4.11
Lead capture	Forms, CTAs, landing & thank-you pages	Per offer.	Pro & Ent	MH-5.01
Segmentation	Core segments	Persona, lifecycle, engagement, customers, suppression.	Pro & Ent	MH-5.02

AREA	ITEM	DETAILS	TIER	TASK
Automation	Nurture workflows & emails	Per persona / offer.	Pro & Ent	MH-5.02
Automation	Lead scoring	Fit + engagement score; MQL threshold.	Pro & Ent	MH-5.02
Automation	MQL handoff	Assignment, notifications, follow-up SLA.	Pro & Ent	MH-5.03
Email	Re-engagement & sunset flows	Keeps the list healthy.	Pro & Ent	MH-5.04
Campaigns	Campaigns, UTMs & ad audiences	Campaign object, UTM conventions, retargeting audiences.	Pro & Ent	MH-5.05
Migration	Rebuild templates & automations	Up to 5 templates; automations active today.	Pro & Ent	MH-5.06
Migration	Parallel send, then switch off the old tool	One parallel send to compare, then cancel the old tool.	Pro & Ent	MH-5.06
Website	Migrate landing pages & blog	Up to 10 landing pages + blog import; redirects set.	Pro & Ent	MH-5.07
Reporting	Marketing performance dashboard	Traffic, leads, MQLs, emails, campaigns.	Pro & Ent	MH-5.09
Reporting	Revenue attribution reports	Multi-touch attribution.	Ent only	MH-5.09
AI	Breeze / AI settings	Brand voice and content tools within the agreed AI terms.	Pro & Ent	MH-5.10
Sales setup	Assign Sales Hub seats	One per rep and manager.	Pro & Ent	SH-4.01
Sales setup	Teams & permission sets	Reps see their own deals; managers see the team.	Pro & Ent	SH-4.01
Sales setup	Connect rep inboxes & calendars	Email logging and meetings booking work for every rep.	Pro & Ent	SH-4.01
Pipelines	One pipeline per sales motion	New business, renewals, partners, as needed.	Pro & Ent	SH-4.02
Pipelines	Stage exit criteria & probabilities	Written down and agreed with the sales lead.	Pro & Ent	SH-4.02
Pipelines	Required properties per stage	Only what the stage really needs.	Pro & Ent	SH-4.02
Leads	Lead status & lifecycle definitions	Agreed with marketing.	Pro & Ent	SH-4.03

AREA	ITEM	DETAILS	TIER	TASK
Leads	Assignment rules	Rotation or territory.	Pro & Ent	SH-4.03
Quotes	Product library	Products and prices the reps quote.	Pro & Ent	SH-4.04
Quotes	Quote templates & e-signature	Branded template; signature flow tested.	Pro & Ent	SH-4.04
CRM migration	Field map approved by the client	Old CRM fields → HubSpot properties.	Pro & Ent	SH-4.05
CRM migration	Import companies, contacts & open deals	With owners mapped.	Pro & Ent	SH-4.05
CRM migration	Import activity history	Where the old CRM allows it.	Pro & Ent	SH-4.05
Sales integrations	Calling and video meetings	HubSpot calling or their provider; Zoom or Teams.	Pro & Ent	SH-4.06
Sales integrations	LinkedIn Sales Navigator	If they use it.	Pro & Ent	SH-4.06
Sales automation	Lead rotation & task queues	New leads land with the right rep and in a queue.	Pro & Ent	SH-5.01
Sales automation	First-touch sequence	Approved by the sales lead.	Pro & Ent	SH-5.01
Sales automation	Qualification properties & playbooks	Same questions on every discovery call.	Pro & Ent	SH-5.02
Sales automation	Closed-won handoff workflow	Notifies onboarding or service with the deal context.	Pro & Ent	SH-5.04
Sales automation	Closed-lost reasons	Required when a deal is lost.	Pro & Ent	SH-5.04
Sales reporting	Pipeline dashboard & forecast	Pipeline by stage, forecast, goals.	Pro & Ent	SH-5.06
Service setup	Assign Service Hub seats	One per support agent and lead.	Pro & Ent	SV-4.01
Service setup	Help desk workspace & business hours	Agents work tickets from one place.	Pro & Ent	SV-4.01
Channels	Support email connected	Replies go out from the help desk.	Pro & Ent	SV-4.02
Channels	Chat & support form	On the website and help pages.	Pro & Ent	SV-4.02

AREA	ITEM	DETAILS	TIER	TASK
Tickets	Ticket pipelines & stages	Matches how the team works today.	Pro & Ent	SV-4.03
Tickets	Priority, category & routing rules	Tickets reach the right agent.	Pro & Ent	SV-4.03
Help desk migration	Import open tickets & history	From the old help desk.	Pro & Ent	SV-4.04
Help desk migration	Import knowledge base articles	Then fix formatting and links.	Pro & Ent	SV-4.04
SLAs	SLA rules by priority	First response and time to close.	Pro & Ent	SV-4.05
Service automation	Ticket automation & snippets	Auto-replies, assignment, saved replies.	Pro & Ent	SV-5.01
Knowledge base	Structure & top 20 articles	Covers the most common questions.	Pro & Ent	SV-5.02
Feedback	CSAT or NPS surveys	Sent after tickets close or on a schedule.	Pro & Ent	SV-5.03
Feedback	Customer success workspace & health scores	If customer success is bought.	Ent only	SV-5.03
Service reporting	Help desk & SLA dashboard	Volume, response times, SLA hits, CSAT.	Pro & Ent	SV-5.04
